

Progress and status

OPERATIONS

- Additional planned roof and rib support actioned between 185m and 195m
- Services installed up to 258m

FORENSICS

- Successfully completed from 170m – 278m

PERSONNEL

- Seven new mine workers employed by 10 February
- Moved to two shifts 10 February

CHALLENGES


- Availability of underground specialist equipment
- Bolting delays based on condition of roof structure and existing bolts

GOALS

- New mine workers' inductions and training completed
- Recover to 400m by 28 February

▲ Tracking ahead of time ● Tracking on time ■ Tracking delayed due to extenuating circumstances

Drift recovery progress

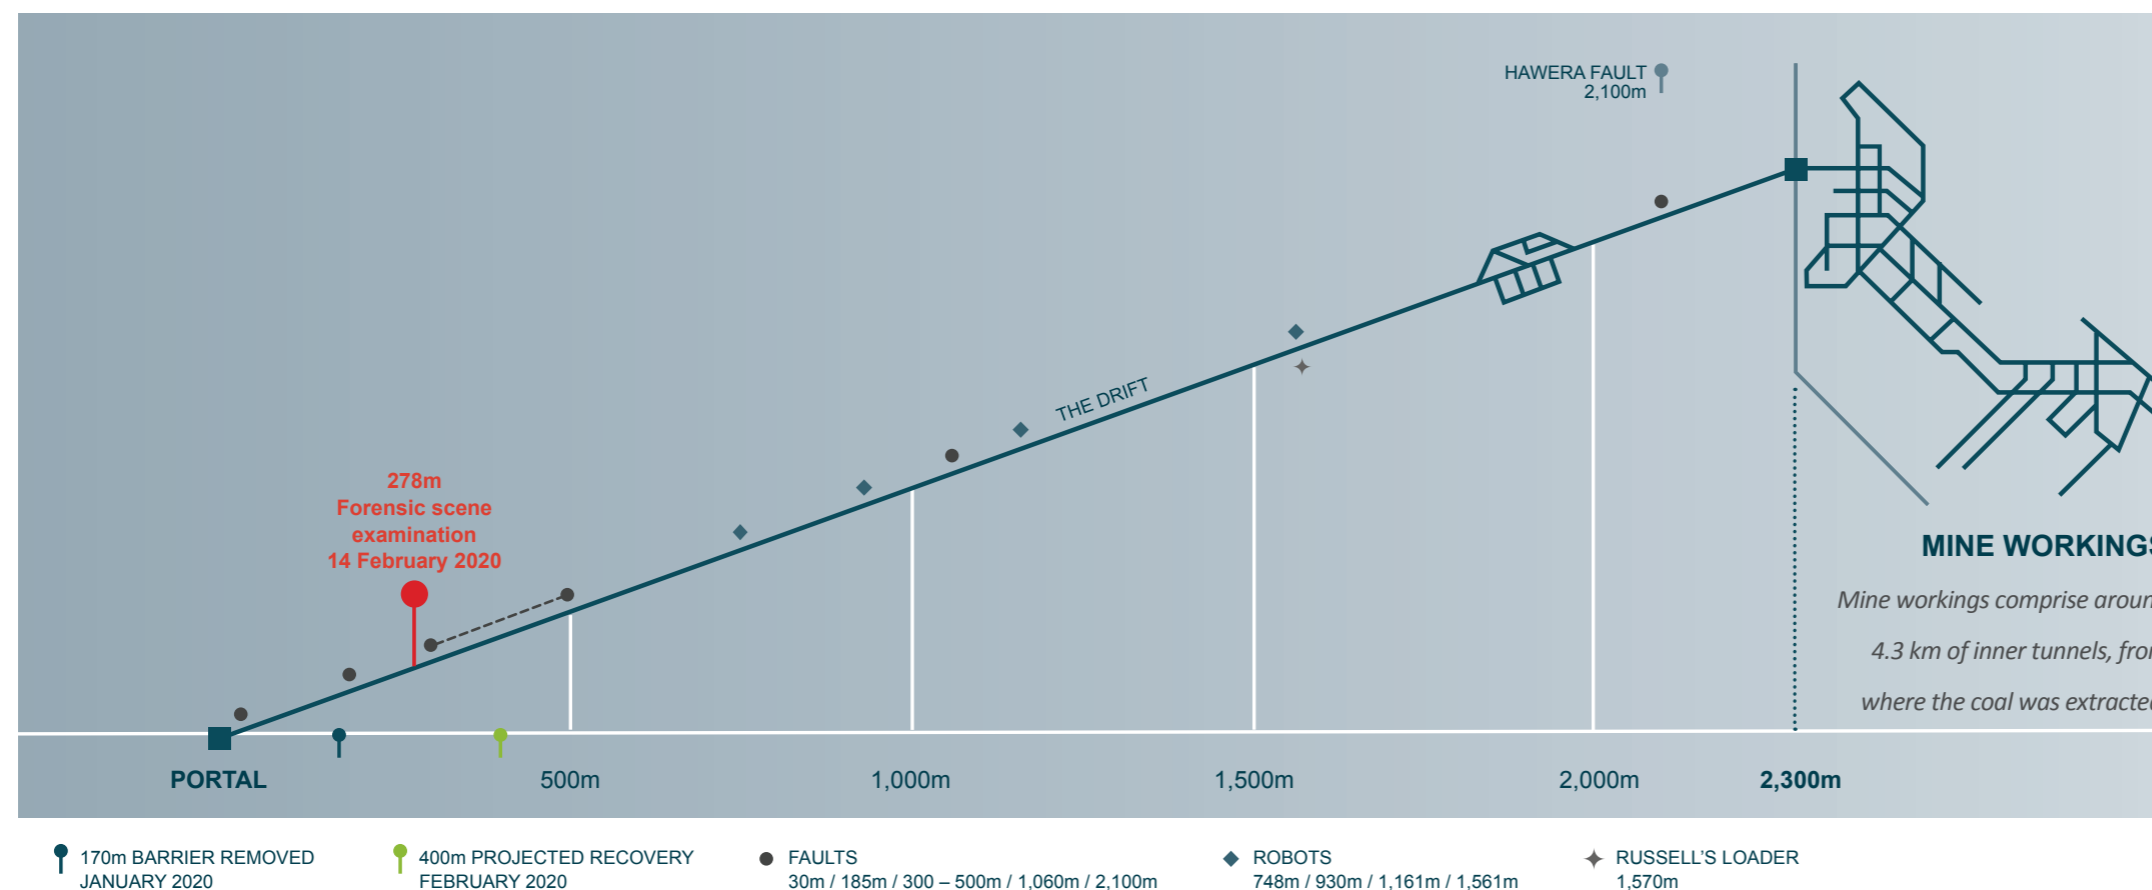

Six
WorkSafe site visits



278m
Progress Reconnaissance barrier moved to 278m



On the hill
Hydro line installed to power comms into PRDH54

Sequence of events timeline

